

DigitalWinch for FlyTrack Logistics

Enterprise Onboarding & Customer Success Plan

90

DAYS
rollout window

14

DEPOTS
nationwide scope

30%

TARGET
fewer delivery exceptions

DigitalWinch × FlyTrack Logistics


Group 1's tailored onboarding strategy for FlyTrack Logistics — built to support rollout, adoption, and measurable customer success outcomes.

WHAT THIS PRESENTATION COVERS

- 1 Case context and customer challenge
- 2 Tailored onboarding strategy
- 3 Success metrics, risks, and governance
- 4 Recommended path to adoption and renewal

THE JOURNEY

Four stages to customer success



● TASK 1

Discovery & Stakeholder Mapping

Junior CSM | January 2026 | ₦85M Contract — 10 stakeholders. 4 tiers. One rollout that cannot fail.

10

Stakeholders Identified
Across all departments and regions

4

Tiers Mapped
Power/Interest quadrant framework

3

Risk Flags Raised
Critical threats to adoption

₦85M


Contract Value
Zero margin for error

The Stakeholder Register

Name / Role	Department	Influence	Interest	Quadrant
Faith Oluchi — CEO	Executive	★★★★★	★★★★	Key Player
Nneka Okoh — CFO	Finance	★★★★	★★★	Manage Closely
Chidinma Grace — Ops Director	Operations	★★★★★	★★★	Manage Closely (SKEPTIC)
Ritty Williams — IT Manager	IT	★★★	★★★	Monitor
Faith Ossai — HR Manager	HR	★★★	★★★★	Keep Informed
Alhajia Aisha Zakari — Lead Supervisor	Operations	★★★	★★	Monitor (Hidden Asset)
Judith Ndineze — Cameroon Coordinator	Operations	★★★	★★	Monitor
Angela Orjiuzo — HQ Finance Team	Finance	★★	★★★★	Keep Informed
13 Depot Supervisors	Operations	★★	★★	Monitor
Depot Staff (Ground Level)	Operations	★	★★	Monitor (Indirect)

Power / Interest Grid — 4 Quadrant Summary



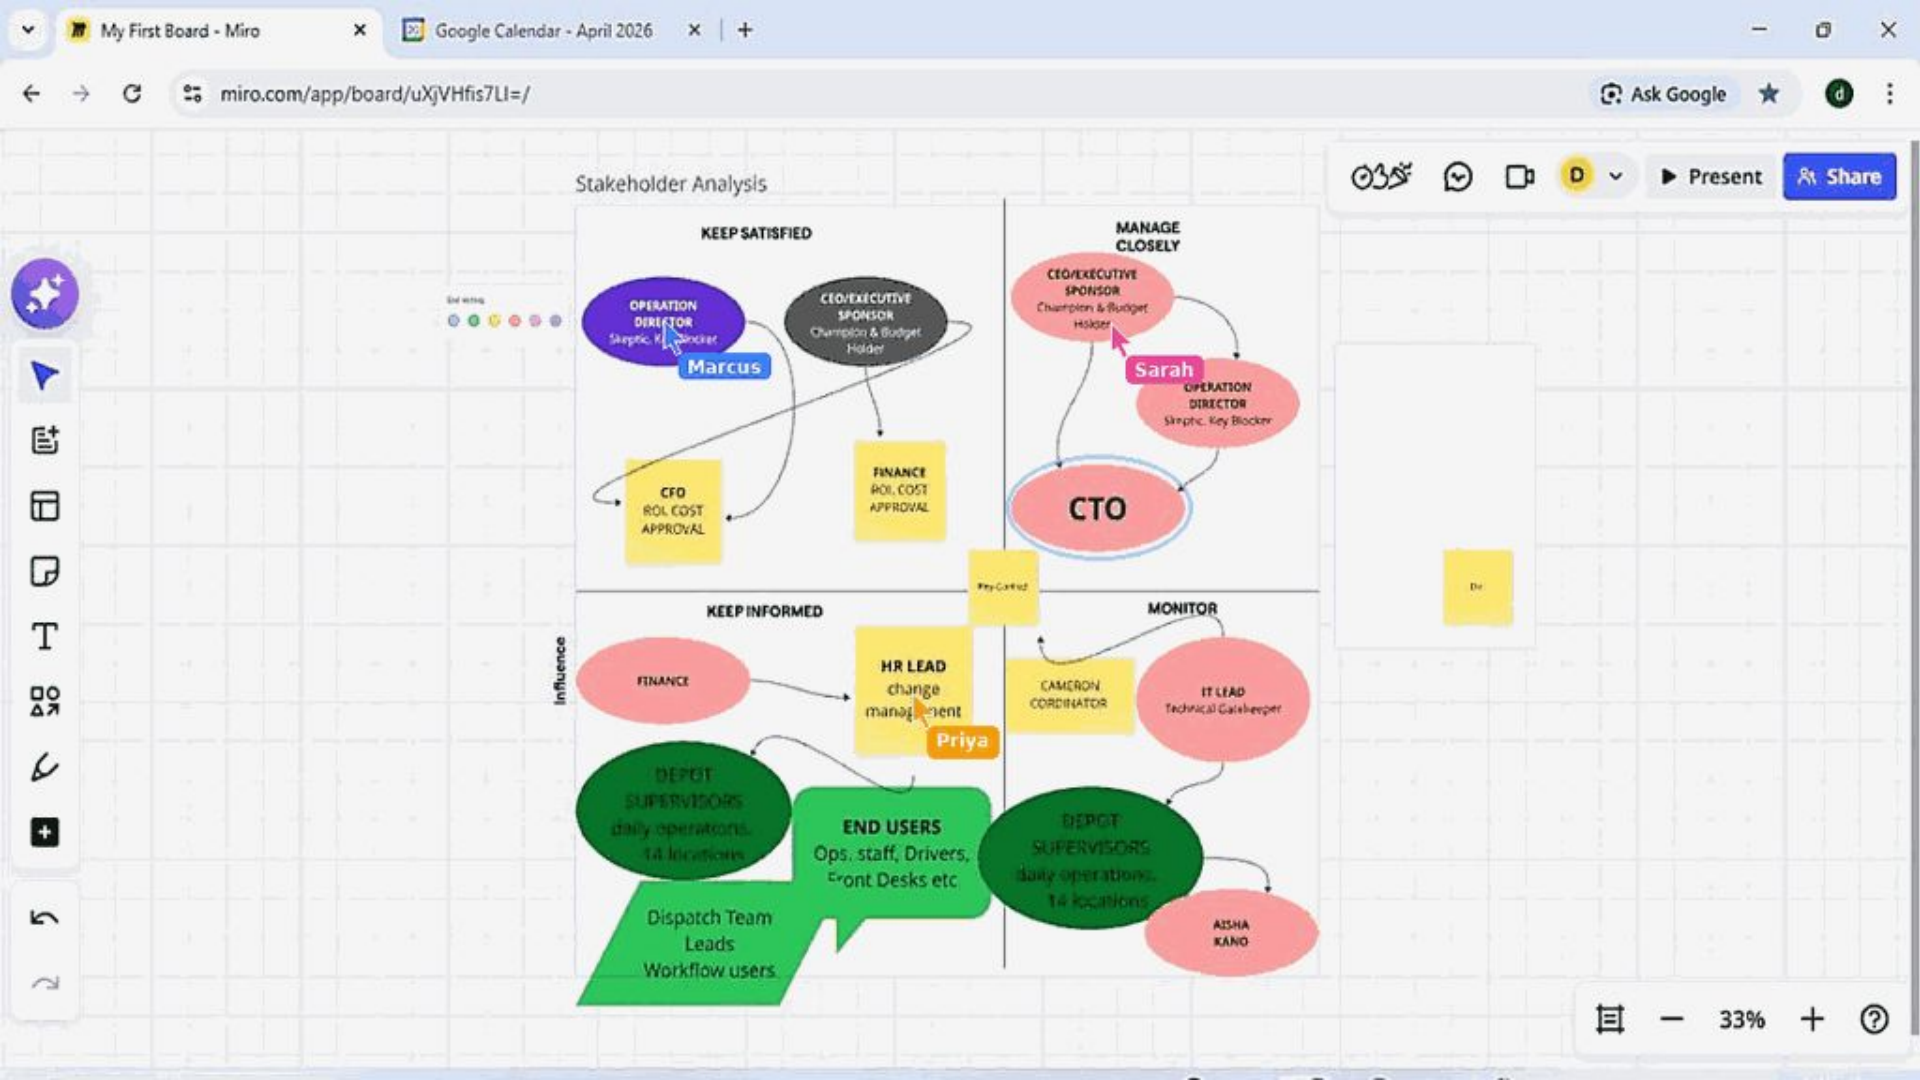

Communication Strategy & Managing the Skeptic

Every stakeholder. One tailored strategy. No surprises.

Communication Strategy at a Glance

Stakeholder	Channel	Frequency	Format	Goal
CEO — Faith Oluchi	Email via EA + monthly call	Bi-weekly	3-bullet milestone summary	Milestone confidence. Never surprised.
CFO — Nneka Okoh	Email + 1 intro call	Monthly	RAG status report (R/A/G)	Financial visibility. ROI evidence.
Ops Director — Chidinma Grace	Call + WhatsApp	Weekly (Wed 9am) + Fri data	1-page KPI summary	Trust through proof. Co-pilot, not passenger.
IT Manager — Ritty Williams	Email + Thursday call	Weekly Mon list + Thu 2pm	Numbered task list with time estimates	Protect his 4hrs. No overruns.
HR Manager — Faith Ossai	Email + scheduling call	Wk 2 call then monthly	Training brief + calendar schedule	Coordinate depot training. 2-week notice minimum.
Aisha Zakari (Kano)	WhatsApp + call	Wk 1 call, weekly WhatsApp	Short voice notes / informal text	Win her = unlock all 13 supervisors.
Judith Ndineze (Cameroon)	Email + call	Wk 2 call, monthly	Structured bilingual email (French & English) + Cameroon plan section	Cameroon not an afterthought.
HQ Finance — Angela Orjiuzo	Email + group demo	Wk 2 demo, monthly check-in	Live demo + before/after one-pager	Activate automation. Turn into champions.
13 Depot Supervisors	Call + WhatsApp group Meeting	Weekly group update	Short text / voice note (Hausa, Pidgin where needed)	Reduce fear. Build confidence pre go-live.
Depot Staff	Via supervisors (indirect)	Managed through supervisors	Visual guides + short demo videos	Silent adoption. Train the trainer.

Managing the Skeptic: Ops Director Chidinma Grace

⊙ **RISK LEVEL: HIGH** — If she disengages, depot supervisors follow her lead and adoption collapses silently.

Stakeholder Profile

Influence: 5/5 | Interest: 3/5

KPI Target: 30% reduction in delivery exceptions

History: ERP failure caused 2-week shutdown

Style: Data-first. Anti-PowerPoint. Direct. Prove it, don't present it.

30-Day Trust-Building Arc

1

Week 1 — Acknowledge

Reference ERP history in first email. No overselling. Acknowledge concerns directly in writing. Do not send a PowerPoint.

2

Week 2 — Deliver

Keep first promise visibly. Send Friday 1-page KPI summary as committed. She watches whether you do what you said.

3

Week 3 — Involve

Invite her to on-site visit at Kano depot. Ask her opinion on Phase 1 depot selection. Make her a co-pilot, not an audience.

4

Week 4 — Prove

Show first KPI data point — however small. Directional data beats no data. -8% delivery exceptions = evidence.



DO

- Send Friday 1-pager every week without being asked
- Reference her 30% exception reduction KPI in every update
- Invite her to observe on-site
- Ask her opinion before announcing decisions



DON'T

- Never send a PowerPoint
- Never miss a Wednesday call without advance notice
- Never make a promise you cannot keep in 7 days
- Never CC her on operational noise

+ Create

April 2026

5	M	T	W	T	F	S
29	30	31	1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	1	2
3	4	5	6	7	8	9

Search for people

Booking pages +

My calendars ^

- ☒ digitalwinch
- ☐ Birthdays
- ☒ Tasks

Other calendars + ^

SUN 29	MON 30	TUE 31	WED Apr 1	THU 2	FRI 3	SAT 4
	8:52am REPLY receive 10:17am REPLY receive 2 more	9:20am REPLY receive 2pm Tuesday Check- 3 more	8:30am Email: Week 1 9am Prepare rollb	9am Intro Call x Ops I 10am Email Follow-up 2 more	11am Live demo — wc 2pm Email Follow-up: 3pm Intro Call x CFO	
5	6	7	8	9	10	11
	9am Check-in Call x 10am Depot WhatsApp	- Due: Week 2 review I 10am Email Update x 3 more	8:30am Email x IT Ma 9am WhatsApp x Dep 11am Call x HR: Traini	9am Call x Ops Dir. — 9am Email x CEO: Bi- 10:15am Email Follow	2pm Friday check-in	
12	13	14	15	16	17	18
	8am Stakeholders x C 2pm On-site debrief	9am Email x IT Manag 10am WhatsApp x De 12pm WhatsApp: Dire	8:30am Email x IT Ma 9am WhatsApp x Dep	9am Check-in Call x 10am Email Follow-up 2pm Email x CMR: Ca	2pm Regular check-in 3pm Email x Finance	
19	20	21	22	23	24	25
	6 pending tasks 8am Stakeholders x C	9am Report Brief x Cl 10am Email x CEO: Bi 11am 30-day Review				
26	27	28	29	30	May 1	2

3 Risk Flags the 30-Day Plan Must Address

● Risk 1 — Chidinma Grace (Ops Director)

Threat: Withdraws support → depot adoption collapses silently across all 13 supervisors.

Mitigation: Weekly calls, data-first updates, quick win by Day 14. Make her a co-pilot from Week 1.

■ Risk 2 — Judith Ndineze (Cameroon)

Threat: Cross-border complexity, bilingual staff, historically deprioritised → missed in 90-day deadline.

Mitigation: Dedicated Cameroon plan, timeline flexibility. Flag to CEO before Day 30.

■ Risk 3 — Aisha Zakari (Kano)

Threat: Informal resistance spreads to all 13 supervisors without a single direct conversation.

Mitigation: Kano as flagship pilot. Win her first. If she endorses publicly in the WhatsApp group, adoption cascades without managing each supervisor individually.

The Communication Pyramid — How It All Connects



Every layer feeds the next. What you tell the executive layer shapes what supervisors believe. What supervisors say shapes what depot staff do.

TASK 2

FlyTrack Logistics

Custom 30-60-90 Day Onboarding Framework

CLIENT

FlyTrack Logistics

CONTRACT VALUE

¥85 Million p.a.

DEPOTS

14 Depots

TIMELINE

90 Days

Earn the right to expand · Evidence before scale · 90 days to operational ownership


1 FlyTrack Context & Key Constraints

FlyTrack Logistics is a 1,200-person road-freight company operating 14 depots across Nigeria and Cameroon. Signed to a ~~N~~\$85 million annual contract with DigitalWinch, FlyTrack's primary objective is a 30% reduction in delivery exceptions within six months. Every element of this onboarding framework is a direct response to the six constraints surfaced at kick-off — not a generic SaaS template applied to a logistics company.


Constraint	Why It Matters	Framework Response
IT Manager: 4 hrs./week	Any implementation requiring more than 4 hours per week will stall — repeating the conditions that caused the previous ERP failure.	CSM absorbs all configuration. IT involvement is limited to SSO (2.5 hrs., one-time) and validation tasks only.
14 geographically dispersed depots	Simultaneous rollout to all 14 depots creates unmanageable support load, inconsistent adoption, and no learning loop.	Phased wave model: 2-depot pilot, then 6, then remaining 6. Each wave informs the next.
Low digital literacy at depot level	Generic training overwhelms basic-literacy supervisors. They revert to WhatsApp and phone calls within days.	Role-segmented training; Hausa/English/French materials; laminated visual job aids; Digital Champion per depot.
Failed ERP — 2-week operational shutdown	FlyTrack's staff and leadership are primed to distrust new software. A big-bang go-live would trigger institutional resistance immediately.	Pilot-first approach. No single failure can cascade. Visible quick win delivered to Operations Director by Day 28.
CEO mandate: all 14 depots live in 90 days	Aggressive timeline creates pressure to move fast. Moving fast without structure repeats the ERP failure.	Milestone gates between phases ensure quality is not sacrificed for speed. Gates are signed, not assumed.
Ops Director KPI: 30% exception reduction in 6 months	Onboarding that doesn't connect to this KPI will lose executive sponsorship — the most common cause of Month 3-6 churn.	Workflow Automation module activated in Phase 1, Day 10. Exception data collected from Day 14. Baseline set by Day 45.



chioma obi

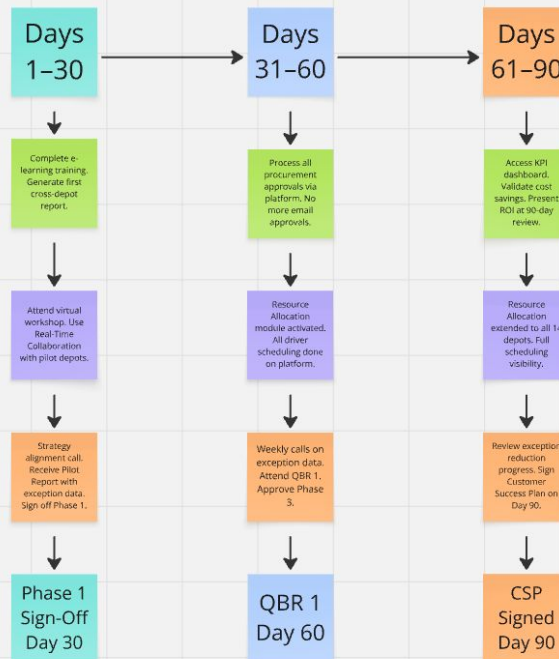

Diagram

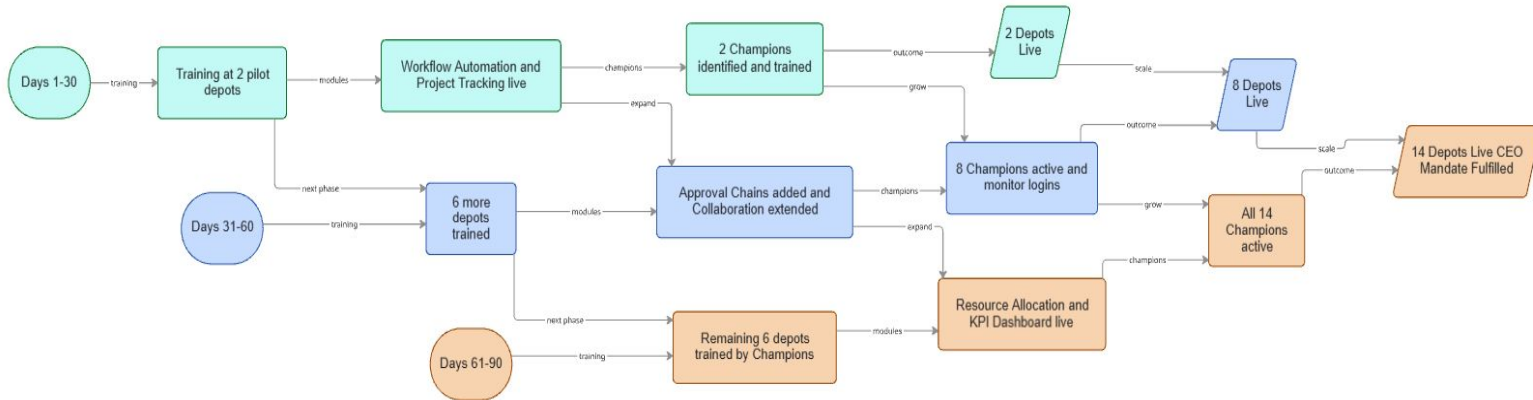

4

Milestones & Success Metrics

4.1 12 Key Milestones Across 90 Days

#	Day	Milestone	Completion Criteria
M1	Day 1	Kick-Off & Stakeholder Alignment	Signed engagement contract; stakeholder register complete; communication calendar approved
M2	Day 7	Platform Configuration Complete	Live tenant environment; all pilot user accounts created; SSO integration live; 3 pre-built tracking templates loaded
M3	Day 10–12	Pilot Depot Go-Live (2 Depots)	Workflow Automation and Project Tracking live; 100% of pilot supervisors trained in English and Hausa; first 5 shipments logged
M4	Day 30	Phase 1 Sign-Off & Wave 1 Approval	80% login rate at pilot depots; 75%+ of exceptions on platform; Pilot Report presented; Ops Director approves Phase 2
M5	Day 40	Wave 1 Depots (6) Progressive Go-Live	All 6 Wave 1 depots live and logging shipments; Digital Champions active in all 8 depots; <15% data entry error rate
M6	Day 43	Automated Approval Chains Activated	3+ approval chain types configured and live; first procurement request approved via platform
M7	Day 50	Delivery Exception Baseline Established	Baseline exception report produced from DigitalWinch data; shared with and acknowledged by Ops Director; delta tracking enabled
M8	Day 60	QBR 1 — 60-Day Business Review	QBR presented to CEO and Ops Director; 10–15% exception reduction evidenced; Phase 3 plan approved; Ops Director NPS score 7/10
M9	Day 75	Wave 2 Depots — All Live	All remaining 6 depots live on DigitalWinch; peer-trained by Phase 1 Champions; 90% of all depot users trained
M10	Day 78	Full Workflow Automation Across All 14 Depots	Workflow Automation and Resource Allocation live in all 14 depots; 0 depots still using informal tracking systems
M11	Day 84	90-Day Exception Progress Report Delivered	Delivery exceptions reduced by minimum 20% vs baseline, on trajectory for 30% by Month 6; KPI Dashboard shared with leadership
M12	Day 90	90-Day Success Review & Renewal Pathway	All 14 depots live and active; health score GREEN; CSP signed; Year 2 renewal conversation initiated; Ops Director NPS 7/10

• TASK 3

Customer Success Plan

DigitalWinch × FlyTrack Logistics

3 SMART Goals · 9 KPIs · 6 Risks · Governance Cadence · 12-Month Value Roadmap

THE MISSION

The Problem

FlyTrack has 14 depots each running their own informal tracking system. Delivery exceptions, missed pickups, delayed routes, damaged consignments have no standardised way to be flagged or resolved.

Result: Exceptions fall through the cracks, performance is invisible, and the Operations Director cannot hit his KPI.

The CSP Goal

This Customer Success Plan ensures FlyTrack achieves a 30% reduction in delivery exceptions within 6 months — the Operations Director's primary KPI.

Every metric, milestone, and governance touchpoint in this plan exists to deliver that single outcome.



SMART GOAL 1 — Exception Reduction

30%

Exception
Reduction
Target

S

Specific

Reduce delivery exceptions across all 14 depots using DigitalWinch workflow automation

M

Measurable

Baseline documented Day 1. Reduction tracked monthly via DigitalWinch analytics dashboard

A

Achievable

Similar logistics clients achieved 20–35% reduction within 6 months post-automation

R

Relevant

Directly tied to Operations Director Tunde Balogun's primary 6-month KPI

T

Time-bound

10% by Day 60 · 20% by Day 120 · 30% by Day 180



SMART GOAL 2 — Workflow Automation Activation

14/14

Depots with
Automation
Active by Day 60

S

Specific

Full activation of workflow automation — exception routing, approval chains, resolution tracking — on all 14 depots

M

Measurable

Activation rate tracked weekly. Target: 100% depots processing at least one workflow per day by Day 60

A

Achievable

Tech Specialist confirmed setup achievable in Phase 2 with current resources if IT involvement is pre-scheduled

R

Relevant

Workflow automation is the #1 reason FlyTrack purchased DigitalWinch. Non-activation = the company-wide churn pattern

T

Time-bound

3 depots by Day 30 · 10 depots by Day 55 · 14/14 depots by Day 60



SMART GOAL 3 — Platform Adoption

75%

Platform Adoption
By Day 90

S

Specific

75% of all depot users logging in and completing at least one workflow action per week

M

Measurable

Login frequency and workflow completion tracked via DigitalWinch user analytics.
Reported weekly per depot

A

Achievable

75% is achievable via Depot Champion programme. 100% not targeted at Day 90 due to literacy and turnover constraints

R

Relevant

Without adoption, exception-reduction data is unreliable — the KPI case for renewal cannot be validated

T

Time-bound

40% by Day 45 · 60% by Day 60 · 75% by Day 90



KPI DASHBOARD — 9 Success Metrics

FlyTrack Raw Database Sheet

Delivery Exception Rate

Baseline: Day 1 baseline

Target: ↓ 30% by M6

Exception Resolution Time

Baseline: Day 1 avg (hrs)

Target: ↓ 50% by M6

Weekly Active Users

Baseline: 0% at Day 0

Target: 75% by Day 90

Automation Activation Rate

Baseline: 0 depots

Target: 14/14 by Day 60

Module Activation Score

Baseline: 0/6 modules

Target: 5/6 by Day 90

Depot Go-Live Count

Baseline: 0 of 14

Target: 14/14 by Day 90

Auto Exception Resolution

Baseline: 0% at Day 0

Target: 80% by Day 90

Stakeholder NPS Score

Baseline: Survey at Day 0

Target: ≥ 8 by Day 90

Training Completion Rate

Baseline: 0% at Day 0

Target: 90% by Day 90



RISK REGISTER — 6 Identified Risks

IT Bandwidth Collapse

P: High

I: Critical

IT-independent design; Tech Specialist leads all implementation; escalation protocol if Chidi unavailable >1 week

Ops Director Withdraws Support

P: Medium

I: Critical

Weekly KPI data sharing; quick win in Week 2; immediate escalation to Nkechi on any disengagement signal

Automation Module Not Activated

P: High

I: Critical

Treated as non-negotiable Day 60 milestone; RACI accountability; emergency Tech Specialist session if behind by Day 50

Depot Supervisor Rejection

P: High

I: High

Depot Champions; Bilingual approach is being adopted here utilizing Pidgin, Hausa/English job aids; gamified adoption recognition; reinforcement training at Day 45

90-Day Deadline Misalignment

P: Medium

I: High

Define 'live' explicitly at Day 3 kickoff; written sign-off from CEO and Ops Director; report against definition consistently

Cameroon Cross-Border Complexity

P: Medium

I: Medium

French & English materials; bilingual Champion by Day 50; 5-day buffer in Wave 3 timeline



GOVERNANCE CADENCE

Every Friday

Weekly Check-in

30 min

Attendees:

CSM + Ops Director

Standing Agenda:

Exception rate · Depot go-live status · Open risks · Action items

Every Wednesday

IT Sync

15 min - 30 min

Attendees:

CSM + IT Manager + Tech Spec

Standing Agenda:

Tech implementation status · Upcoming depot prep · IT decisions.

User Issue → L1 (Internal Triage) → L2 (Technical Resolution) → L3 (Executive Escalation) → Resolution → Feedback Loop

Last Mon of Month

Monthly Business Review

60 min

Attendees:

CSM + Ops Dir + IT Mgr + Nkechi

Standing Agenda:

Full KPI dashboard · Adoption scorecard · Risk register · Next month priorities

End of Month 3 & 6

Quarterly Business Review

90 min

Attendees:


CSM + Nkechi + CEO + Ops Dir + IT Mgr

Standing Agenda:

KPI vs. targets · ROI calculation · Strategic roadmap · Renewal discussion (Month 6)



12-MONTH VALUE REALISATION ROADMAP

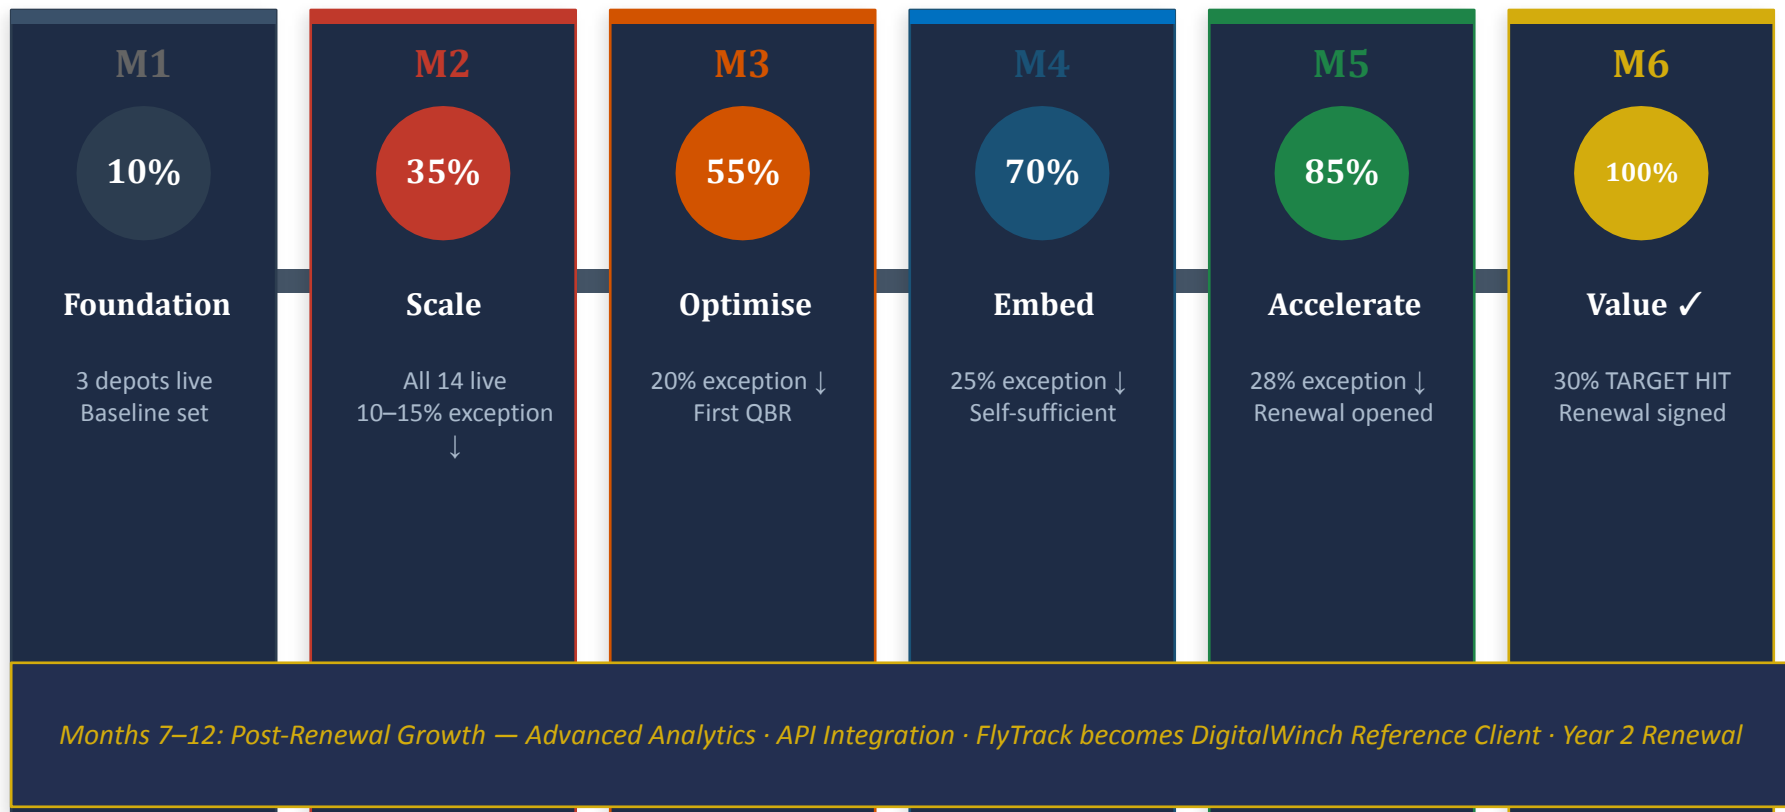



The Outcome

30%

Delivery exception
reduction by Month 6

14/14

Depots live and
automation active by Day
90

75%+

Platform adoption
across all depot users



Renewal conversation
opened from proven ROI

This CSP is not a document. It is a commitment.

• Task 4

HANDLING RESISTANCE & CREATIVE PROBLEM-SOLVING

DigitalWinch × FlyTrack Logistics

Week 3 Crisis · Root Cause Analysis · Email Response · Corrective Action Plan · Creative Solutions



ACTIVE CRISIS — Day 21 · 90-Day Deadline Must Not Move



THE CRISIS — Week 3, Day 21

 Inbound Email — Chidimma Operations Director

Subject: RE: DigitalWinch Rollout — Requesting Pause

I am writing to flag a serious concern. Two of our depot supervisors have come to me saying the DigitalWinch system is too complicated to use.

Given our previous experience with the ERP failure, I am not comfortable continuing this rollout until we have resolved this. I am considering pausing the deployment.

Please advise on next steps.

What's at Stake

 90-day CEO mandate cannot move

 KPI evidence gaps if rollout pauses

 ERP failure trauma re-triggered

 Wave 2 depots not yet live

 Trust destroyed at critical moment

The CSM has 24 hours to respond, prevent the pause, and present a credible corrective plan — without moving the 90-day deadline.



ROOT CAUSE ANALYSIS — 'Too Complicated' Is a Symptom, Not a Cause

01 Interface Overwhelm

Supervisors see the full enterprise platform from Day 1 — all modules, all menus. They only need 2–3 daily tasks. The cognitive load is incompatible with very basic digital literacy.

Evidence: Staff digital literacy ranges from advanced (HQ) to very basic (depot supervisors)

02 Training Format Mismatch

Group classroom training with manuals doesn't work for users who've never used business software. Depot supervisors learn by doing alongside someone — not from documentation.

Evidence: Previous ERP failed — almost certainly used the same top-down training approach

03 Language & Context Gap

Training materials in corporate English are disconnected from how depot supervisors communicate. Hausa-language resources were available but not fully deployed at the struggling depots.

Evidence: DigitalWinch has Hausa training resources — deployment was incomplete

04 Fear of Looking Incompetent

Supervisors who struggle in group settings will not ask for help publicly. They disengage instead. 'Too complicated' masks a deeper reluctance to admit difficulty in front of colleagues.

Evidence: High staff turnover means supervisors feel job insecurity if they appear to be underperforming



THE EMAIL REPLY — Empathetic, Strategic, Data-Led

To: Chidinma Subject: Re: Rollout Pause — I Hear You, and Here Is What We Are Doing

Dear Chidinma,

Thank you for flagging this. I take this seriously — your confidence matters more than hitting a calendar milestone.

I have already spoken with both supervisors this morning. What I heard is not that DigitalWinch is wrong — it is that they were given an enterprise platform when they needed something simple. That is on us, and I am fixing it today.

Here is what I am doing in the next 72 hours:

1. Simplified 3-task view deployed for both supervisors today
2. Depot Champion going to their depots in person tomorrow
3. WhatsApp video guides in Hausa — ready by end of day

The 90-day deadline is still achievable. We have buffer in the schedule. I am asking for 7 days to show you data before we make any pause decision.

You have my full attention on this, Chidinma.

Why This Email Works

Opens with validation

Tunde feels heard before any solution is presented. He doesn't become more entrenched.

Action already taken

'I have already spoken with both supervisors' — the problem is being solved before he reads the email.

Deadline addressed

His political exposure to the CEO is resolved directly — he won't need to explain a delay.

Data, not promises

'7 days to show you data' — the CSM backs confidence with evidence, not reassurance.



CORRECTIVE ACTION PLAN — 14 Days · No Deadline Extension

Deadline Preservation: A 5-day buffer is built into the Wave 1 rollout schedule. Suspending new go-lives for 7 days uses this buffer — the Day 90 deadline does not move.

Within 24 Hours Immediate Stabilisation

- 1 Send empathetic email reply to Tunde — problem acknowledged, solution already in motion
- 2 Call both struggling supervisors directly — listen only, do not train
- 3 Suspend all new depot go-lives temporarily
- 4 Brief Nkechi Okafor — escalate as Level 2 internally

Days 2–3 Root Cause Diagnosis

- 1 1:1 sessions with each supervisor — identify the specific friction points
- 2 Review platform usage logs — find exactly where drop-off is happening
- 3 Survey all active supervisors — is this isolated or systemic?
- 4 Identify Depot Champions available for peer coaching deployment

Days 4–5 Modified Training Deployed

- 1 Deploy 3-Task Protocol — simplified view showing only 3 daily actions
- 2 Create WhatsApp Hausa video guides — 60 seconds per task
- 3 Send Depot Champions to struggling depots for in-person coaching
- 4 Schedule follow-up call with Tunde — present plan with timeline

Days 6–14 Recovery & Momentum

- 1 Daily check-in with struggling supervisors for 7 days post-intervention
- 2 Share daily login data with Tunde — one number, every day
- 3 Resume Wave rollouts once both depots show 3 consecutive active days
- 4 Present full recovery data at next weekly check-in



MODIFIED TRAINING APPROACH — Before vs. After

✗ ORIGINAL APPROACH — FAILED

- ✗ Group training sessions in a meeting room
- ✗ Full enterprise platform shown from Day 1
- ✗ English-language documentation only
- ✗ One-time training — no structured follow-up
- ✗ Supervisors expected to self-navigate after training
- ✗ Errors corrected publicly in front of colleagues

VS


✓ MODIFIED APPROACH — IMPLEMENTED

- ✓ 1:1 shoulder-to-shoulder coaching at the supervisor's own depot
- ✓ 3-Task Protocol — only 3 daily actions visible at first
- ✓ WhatsApp video guides in Hausa — 60 seconds per task
- ✓ Daily check-ins for 7 days post-relaunch
- ✓ Depot Champions provide ongoing peer support
- ✓ Private channels for questions — no public struggle



CREATIVE SOLUTION 1 — The 3-Task Protocol (Non-Standard Innovation)

The Tech Specialist configures a role-specific simplified view for each depot supervisor. They see only 3 tasks. One new task is added per week once the previous tasks are completed with confidence. By Week 4, supervisors are using the full platform — without ever having been overwhelmed.

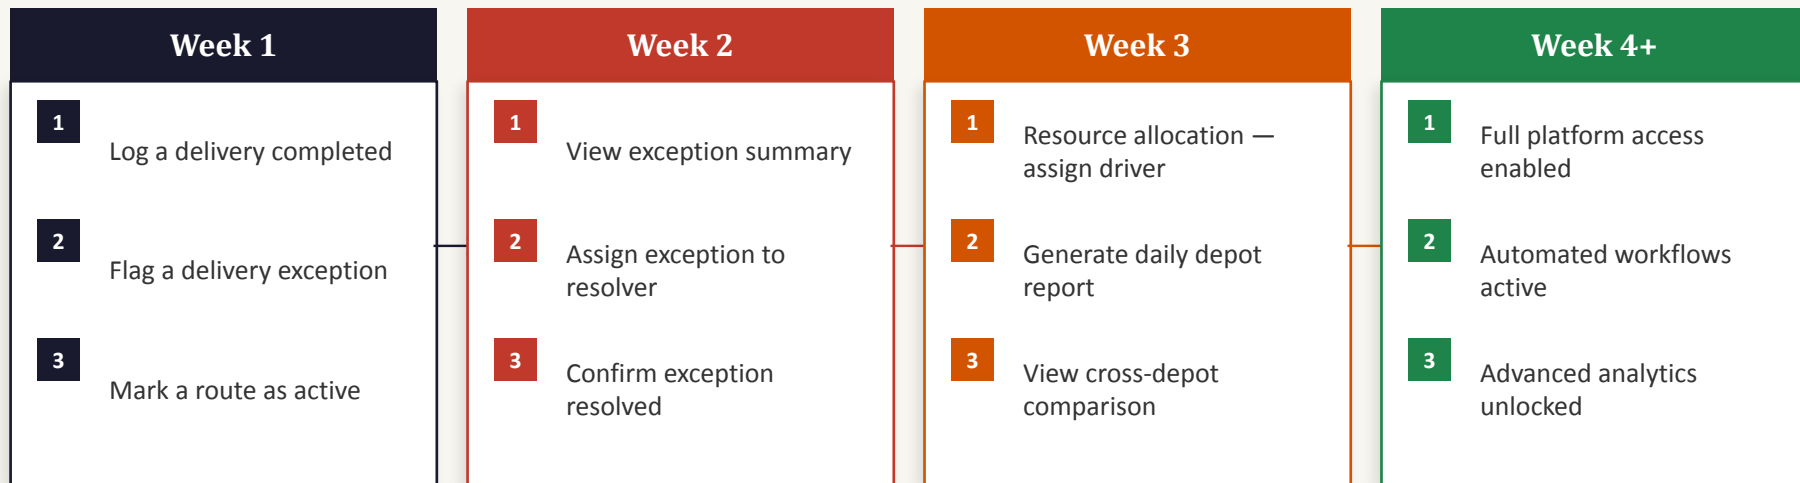

Why This Works:

Enterprise platforms are built for power users. Depot supervisors are not power users. Mobile banking apps like Kuda and PalmPay achieved massive adoption among low-literacy users by launching with 2–3 core functions first. DigitalWinch applies the same progressive complexity principle.



CREATIVE SOLUTION 2 — The WhatsApp Classroom (Non-Standard Innovation)

What It Is

A private WhatsApp group is created for each struggling depot, containing:

- The Junior CSM
- The Depot Champion
- The struggling supervisor

60-second video tutorials are posted showing each task in the supervisor's own depot context — filmed on a smartphone, informal in tone, in Hausa where needed.

Supervisors can rewatch as many times as needed, ask questions without embarrassment, and see their Champion succeeding alongside them.

Why It's Non-Standard



Meets them where they are

WhatsApp is already the dominant business tool in Nigerian road freight. No new app to learn.



Private learning environment

No public struggle. Supervisors ask questions without fear of judgment from colleagues.



Reusable training asset

Videos onboard new staff automatically as they join — directly addressing FlyTrack's high turnover risk.

Precedent: DigitalWinch already has Hausa training resources — WhatsApp delivery makes them available at the moment of need, not just in a training session.



CREATIVE SOLUTION 3 — The Depot Champion Acceleration Fund (Incentive Innovation)



Goal: Accelerate platform adoption across all 14 depots by using positive recognition and healthy peer competition — at **zero cost to DigitalWinch**.

WHAT IT IS



Each week, the FlyTrack depot with the highest **DigitalWinch adoption rate** is featured in FlyTrack's internal communications.

The depot supervisor is congratulated **by name** by the Operations Director.

Other depots are invited to compete for next week's recognition.

EXAMPLE RECOGNITION MESSAGE

“ Congratulations to **KANO DEPOT** for achieving the highest DigitalWinch adoption rate this week!

Great leadership, great teamwork, and driving results for FlyTrack.

— **Chidinma Grace**
Operations Director

”

HOW IT WORKS



1
Adoption data is reviewed weekly from DigitalWinch analytics dashboard.



2
Top performing depot is selected based on adoption rate.



3
Operations Director announces and congratulates the winning depot.



4
Other depots are motivated to improve and compete for next week's recognition.

WHY THIS WORKS



Leverages Positive Peer Pressure

Supervisors compete to be recognised among their peers.



Shifts Mindset from Fear to Pride

From “avoiding failure” to “winning recognition”.



Zero Cost, High Impact

Uses existing internal communications. No budget required.



Proven by Research

Salesforce research shows public recognition drives adoption faster than training alone.



Builds a Culture of Excellence

Celebrates good performance and encourages consistent improvement.



THE RESULT: A motivating, respectful, and competitive environment that drives faster adoption, stronger engagement, and better results — without adding cost or complexity.



RECOGNITION FUELS ADOPTION.
Champions inspire change.



EMOTIONAL INTELLIGENCE + DEADLINE PRESERVED

Emotional Intelligence in Training Design

Normalise the Struggle

Every 1:1 coaching session opens with: 'Everyone who tried this for the first time found it hard. You are not behind.' This removes the shame that prevents asking for help.

Celebrate Small Wins

'You just logged your first delivery on DigitalWinch. That is a real achievement.' Positive reinforcement builds confidence faster than any training manual.

Private Before Public

No supervisor demonstrates a skill in front of colleagues until they personally confirm they feel ready. Confidence must precede visibility.

How the 90-Day Deadline Is Preserved

Days 1–5

Pause on new go-lives · Corrective plan deployed

Days 6–7

Both supervisors show 3 consecutive days of active use

Days 8–10

Wave 1 go-lives resume using 5-day schedule buffer

Days 11–14

Wave 2 progresses — no net delay to wave completion

Day 90

All 14 depots live — CEO mandate fulfilled on schedule



What This Response Proves



Empathy

Tunde felt heard
not managed



Strategy

Root cause found
not symptoms treated



Innovation

3-Task Protocol &
WhatsApp Classroom



Execution

14-day fix, no
deadline extension

A great CSM does not just prevent a pause. They turn a crisis into a trust-building moment.

Task 5

Reflection & Strategic Recommendation

A concise final presentation built around the Task 5 memo to Nkechi Okafor.

This section does not repeat Tasks 1–4. It offers a simple, strategic view of what DigitalWinch should change permanently after the FlyTrack case.

These will form recommendations for systemic improvements to DigitalWinch's enterprise onboarding framework.

A strategic memo to Nkechi Okafor recommending systemic improvements to DigitalWinch's enterprise onboarding framework



01 RACI-based governance

By proactively identifying stakeholders, internal champions, blockers, low-engagement users, and key decision-makers, etc with clear roles, we can tailor communication and enablement efforts more effectively.

02 Milestone-driven Time-to-Value (TTV) framework

Clients should progress based on achieving key milestones that ensures they realise value early.

In parallel, each client have their unique business context. Domesticating the onboarding playbook where necessary.

03 Real-time onboarding health scores tracking

Training This would enable us to identify at-risk accounts early and intervene proactively.

04 “Activation Sprint + Embedded Champion” model

Focus on a narrow, high-impact use case to deliver a quick win.

Identify and train internal champions who can drive adoption within their teams.




To: Nkechi Okafor, Head of Customer Success
From: Junior Customer Success Manager
Subject: Systemic Improvements to DigitalWinch's Enterprise Onboarding Framework

Dear Nkechi,

Based on recent outcomes, I have observed that our current onboarding approach is delivering strong initial satisfaction but falling short in driving sustained product adoption. This is reflected by the churn of our customers between months 3 and 6, and a low activation of key modules of Digital Winch's platform. After working with FlyTrack, I identified some unique ideas that I will be recommending. These will give us an onboarding framework that combines accountability, outcome alignment, and early value delivery.

First, DigitalWinch should standardise RACI-based governance for all enterprise accounts, so ownership is clear across implementation, training, communication, escalation, and success measurement. Many onboarding challenges stem from misaligned or disengaged stakeholders and ambiguity around roles, particularly in complex organisations. By proactively identifying internal champions, blockers, low-engagement users, financial influencers, etc, we can tailor communication, training, and post-onboarding efforts more effectively.

Second, I recommend introducing adopting a milestone-driven Time-to-Value (TTV) framework, with adoption checkpoints tied to feature usage rather than activity timelines. Our current 30-60-90 Onboarding model assumes linear progress of activities, but enterprise onboarding is rarely predictable, especially in environments with varying digital maturity or multilingual capacities. Progress for every client should now depend on achieving key adoption milestones, such as “ first workflow automated ” or “first cross-department collaboration executed.” This ensures no client advances without building the necessary foundation, reducing the risk of partial or poor adoption, and a later disengagement. To add to this, we can ensure our playbook is customised for every customer, to suit their unique business context.

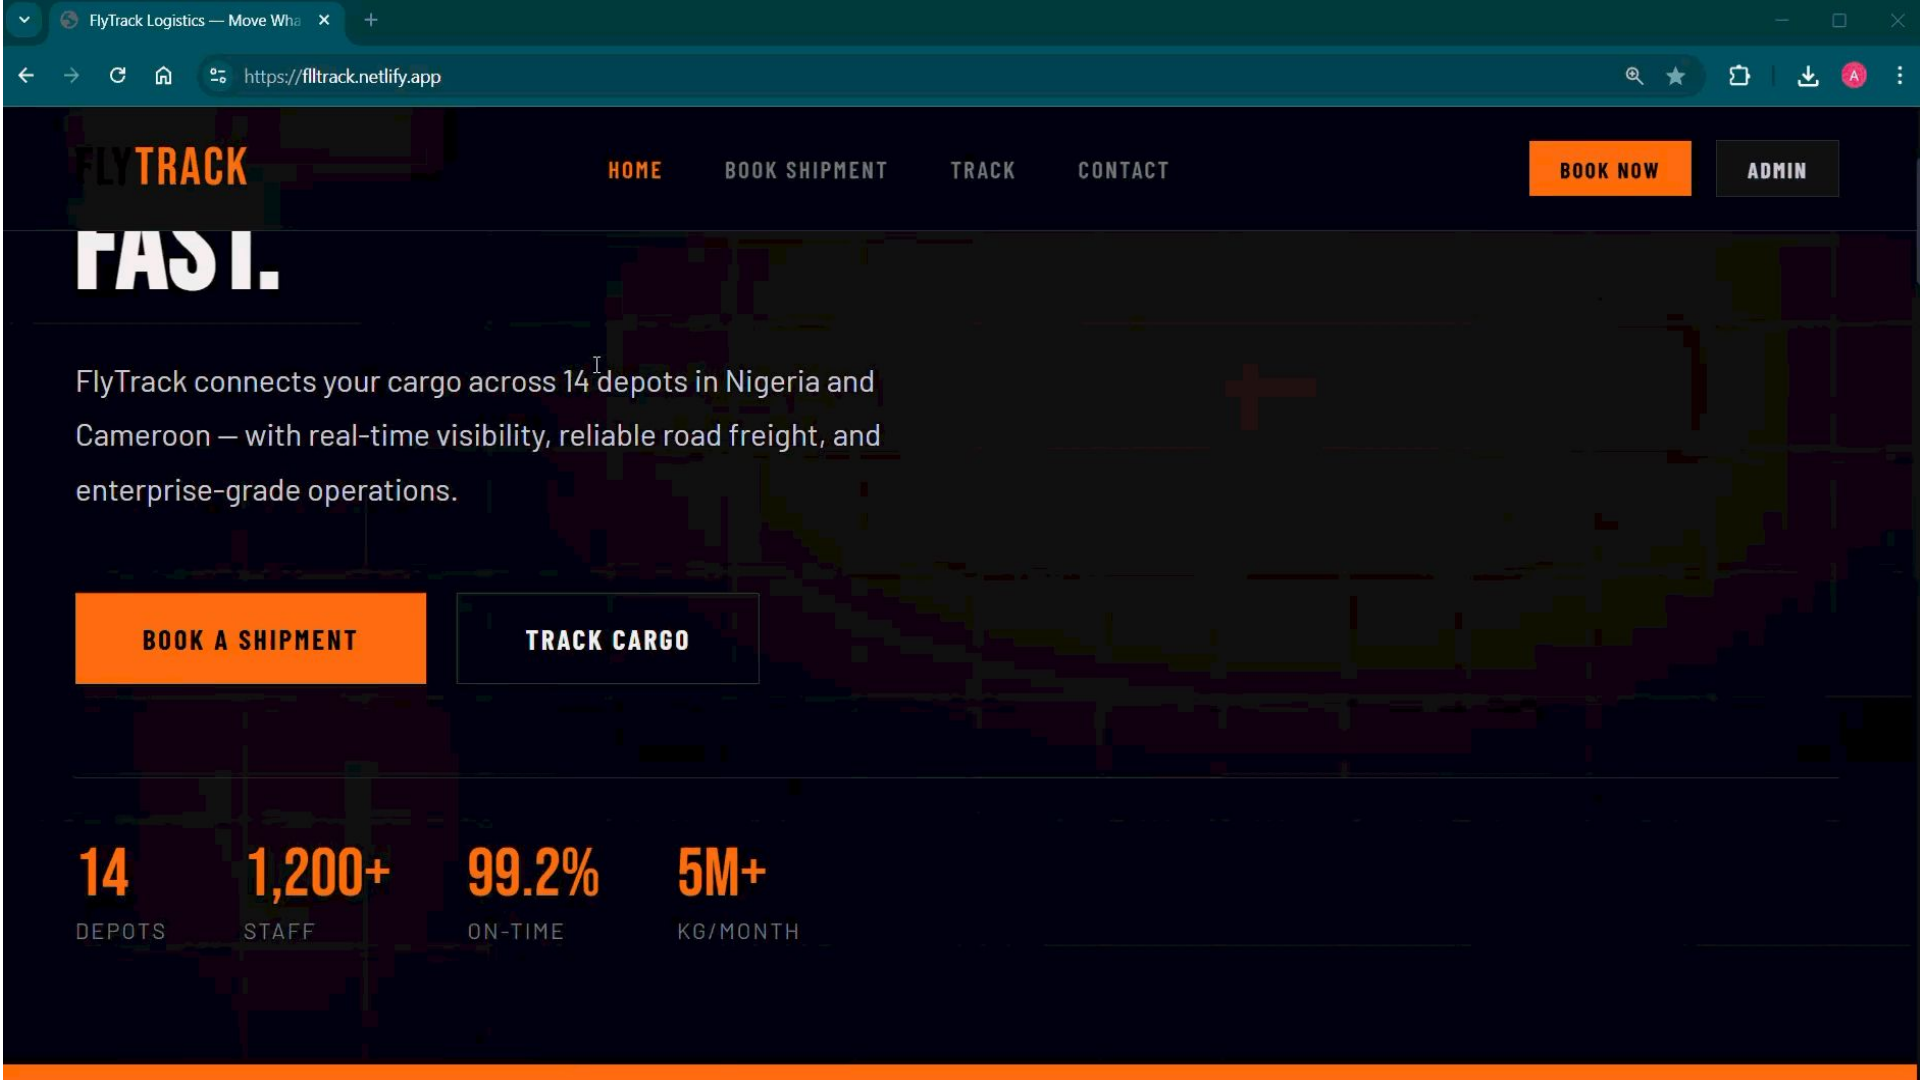

FLYTRACK

HOME

BOOK SHIPMENT

TRACK

CONTACT

BOOK NOW

ADMIN

FAST.

FlyTrack connects your cargo across 14 depots in Nigeria and Cameroon — with real-time visibility, reliable road freight, and enterprise-grade operations.

BOOK A SHIPMENT

TRACK CARGO

14

DEPOTS

1,200+


STAFF

99.2%

ON-TIME

5M+

KG/MONTH

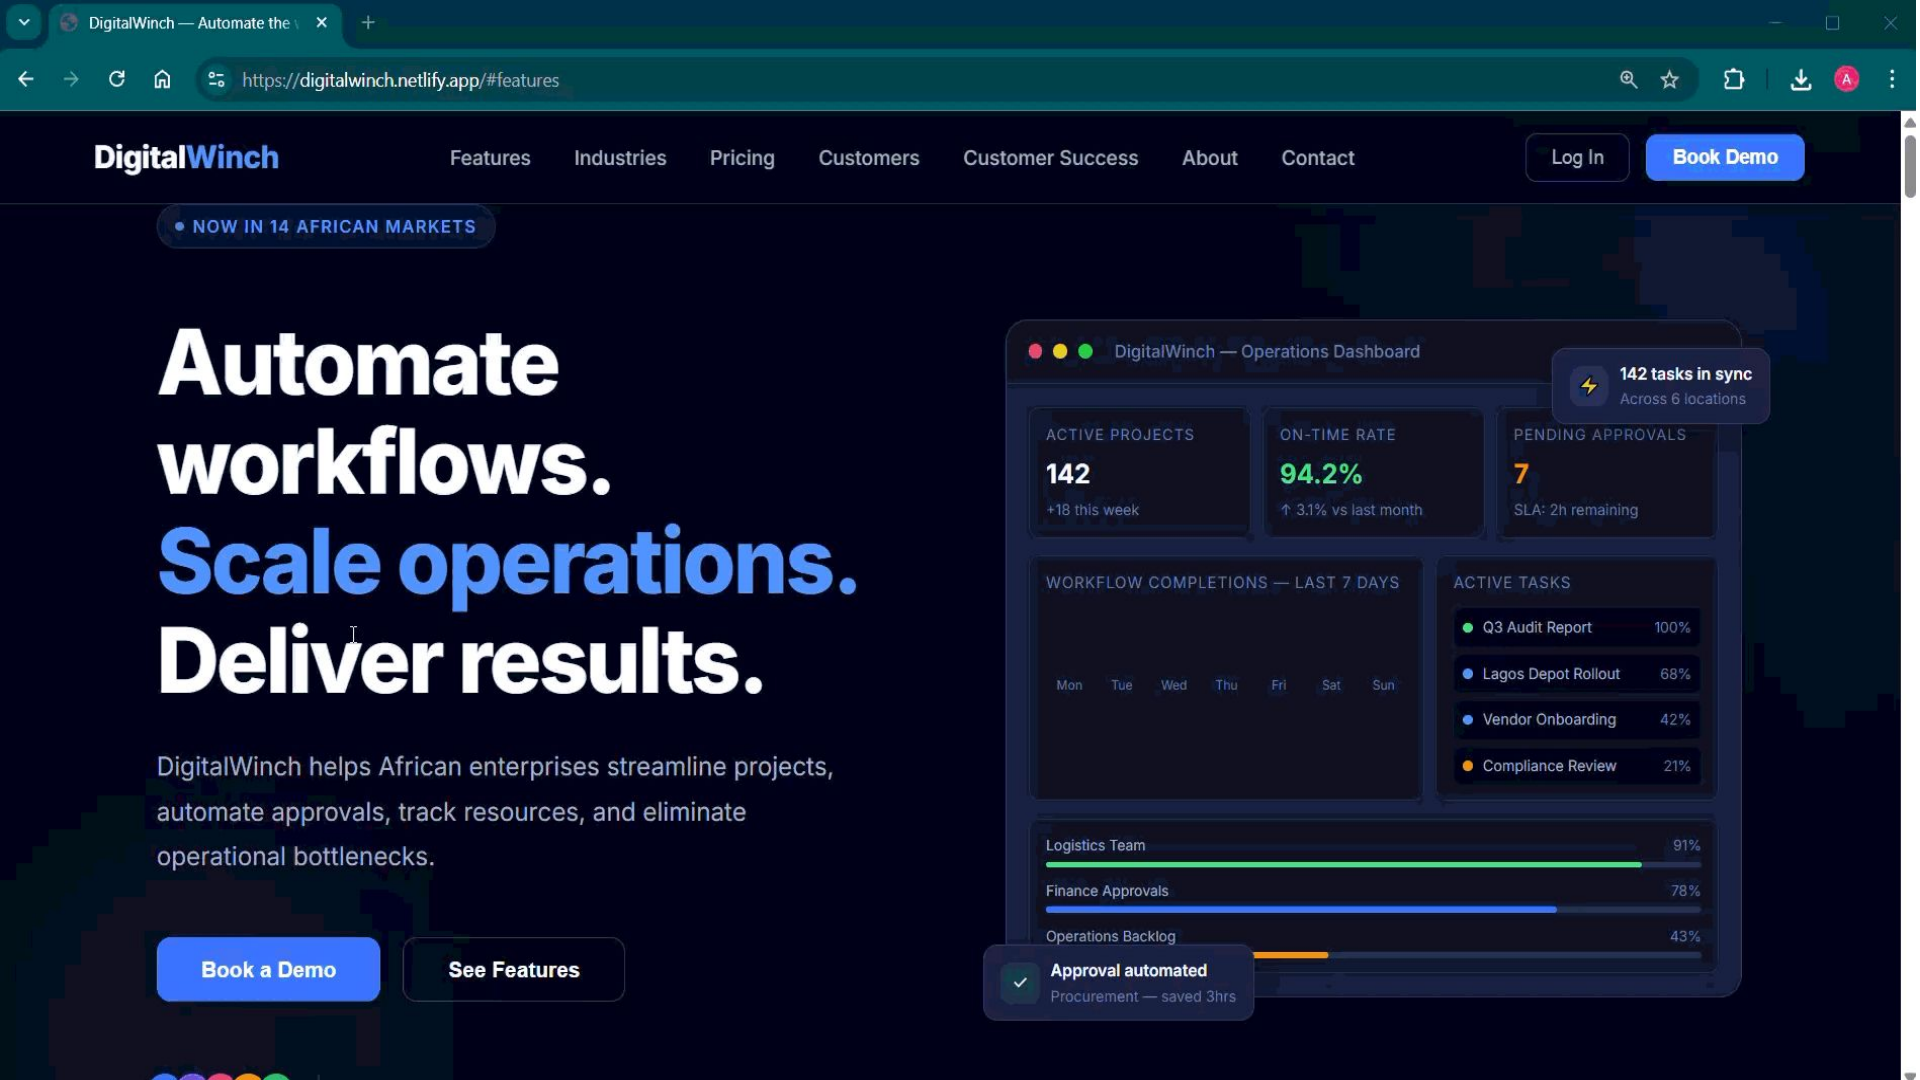

• NOW IN 14 AFRICAN MARKETS

Automate workflows. Scale operations. Deliver results.

DigitalWinch helps African enterprises streamline projects, automate approvals, track resources, and eliminate operational bottlenecks.

Book a Demo

See Features

DigitalWinch — Operations Dashboard

142 tasks in sync
Across 6 locations

ACTIVE PROJECTS

142

+18 this week

ON-TIME RATE

94.2%

↑ 3.1% vs last month

PENDING APPROVALS

7

SLA: 2h remaining

WORKFLOW COMPLETIONS — LAST 7 DAYS

Mon Tue Wed Thu Fri Sat Sun

ACTIVE TASKS

- Q3 Audit Report 100%
- Lagos Depot Rollout 68%
- Vendor Onboarding 42%
- Compliance Review 21%



Approval automated

Procurement — saved 3hrs

HubSpot CRM - Live Demo

The screenshot displays the HubSpot CRM interface, specifically the Deals pipeline. The top navigation bar includes a search bar labeled "Find or Ask", an "Upgrade" button, and various utility icons. The main header shows the "Deals" section with a dropdown menu and an "Add deals" button. Below this, there are tabs for "All deals" and "My deals". The "Sales Pipeline" dropdown is set to "All deals". The main content area shows a Kanban-style view of the sales pipeline with columns for different stages: "Appointment Scheduled", "Qualified To Buy", "Presentation Scheduled", "Decision Maker Bought-In", "Contract Sent", "Closed Won", and "Closed Lost". The "Closed Won" column is currently selected, showing two deals. Each deal card displays the company name, creation date, last activity date, and value.

Find or Ask **Upgrade** **Assistant** **DIGITALWINCH**

Deals **Add deals**

All deals **My deals** **Sales Pipeline**

Deal owner **Create date** **Last activity date** **Close date** **Advanced filters**

Appointment Scheduled **Qualified To Buy** **Presentation Scheduled** **Decision Maker Bought-In** **Contract Sent** **Closed Won** **Closed Lost**

Onboard FlyTrack Logistic
04/21/2026
04/08/2026
\$85,000,000
Digital Winch
\$5

Onboard FlyTrack Logistic
04/21/2026
04/08/2026

ONBOARDING & TRAINING SESSIONS × FLYTRACK



loom

Search for people, tags, folders, Spaces, and Looms


Upgrade



Videos

Upload date ▼

Newest to Oldest ▼



DW Digital Winch 7 months

French Training Session for Cam Flytrack

👁 0 💬 0 🌟 0



DW Digital Winch 10 months

Hausa Training Session for Flytrack

👁 0 💬 0 🌟 0

Board | List | DigitalWinch Trailblazers (Group 1) | Board | Discovery & Stakeholder Mapping

app.clickup.com/9015140612/v/b/S-901515666930-2

Google Gmail YouTube Maps News Translate EST to Lagos Time C... Farmcrowdy Limited Facebook Ads Manager - Man... Business Settings Flexjobs 39 All Bookmarks

DigitalWinch Trailblazers (Group 1) Search ClickUp

Home

ClickUp needs your permission to send notifications [Enable](#) [Remind me](#)

FlyTrack / Discovery & Stakeholder Mapping

Agents Automate Ask AI Share

Overview Board List + View

Status

+ Task

COMPLETED 5

+ Add group

Task 1 — Stakeholder Identification

1 subtask

Task 3 — Stakeholder Map (Visual)

CSM / TAM Group

Enterprise Workspace

CHANNELS

general

new-channel 2

it-managers

hq-finance 4

senior-management 7

team-meeting

social

DIRECT MESSAGES

C chigozie

G Gladys Ehikwe 1

F Faith Ifunanya 1

C Chioma Ruth Obi

O Onyii Chuks

it-managers

12 members

Today — April 24, 2026



chigozie IT MANAGER 9:02 AM

👋 Good morning IT Managers! Daily standup reminder — systems check at **9:30 AM**.



Gladys Ehikwe IT MANAGER 9:05 AM

Confirmed ✅ — patching window for servers 12-15 is **tonight 11 PM–2 AM**. Tickets raised.



Faith Ifunanya IT MANAGER 9:08 AM

VPN latency issues reported by [@hq-finance](#) team. Investigating now — likely Lagos datacenter routing.



Chioma Ruth Obi IT MANAGER 9:11 AM

Escalated to [@senior-management](#) — SLA breach risk if not resolved by EOD. Dashboard updated 🟡



Onyii Chuks IT MANAGER 9:14 AM

New hardware request from [@hq-finance](#): 8× workstations needed for Q2 hire batch. Procurement form submitted.

... chigozie is typing...



Root cause

Me

Search or start new chat

- DigitalWinch CSM...** 22:04
Release Strategy...
- Xochil O.** 21:58
Ok noted, thanks!
- FlyTrack Team** 21:40
Meeting at 9am tmrw
- joyful Gladys** 21:46
Sent a document
- Thecla Chisom** 21:22
Ok how do we go about it
- Onboarding Group** 21:06
New Call at 6/7

DigitalWinch CSM...
Thecla Chisom, joyful Gladys, FlyTrack Team, shortletbvdée 4/5

Thecla Chisom

Good evening dearest 🌙

21:16

I want us to finalise on the onboarding demo.

7/7 21:26

Thecla Chisom

Ok how do we go about it

21:22

Chlöma Ruth O

Hello everyone 👋

21:26

Chlöma Ruth O

Please have we done the onboarding video?
@all

21:26

shortletbvdée

Type a message



↶

👉

□

○

✎

T

🔗

📌

KEEP SATISFIED

OPERATION DIRECTOR
Skeptic, Key Blocker

CEO/EXECUTIVE SPONSOR
Champion & Budget Holder

CFO
ROI, Cost Approval

FINANCE
ROI, Cost Approval

CEO/EXECUTIVE SPONSOR
Champion & Budget Holder

↶ Priya

↶ Sarah

↶ Cameron

↶ Marcus

↶ Aisha

Thank you.

Group 1 appreciates your time and attention.

Questions, feedback, and comments are welcome.

PREPARED BY GROUP 1 TEAM

